

PROJECT PLANNING PHASE

Metro Ticket Generating System in ServiceNow

Date	21 September 2026
Roll Number	238W1A4259
Project Name	Metro Ticket Generating System in ServiceNow
Maximum Marks	2 Marks

Project Planning Phase

Planning for this project uses standard Scrum terms: an **Epic** is a large piece of work, a **Story** is a smaller task within it, a **Story Point** is a relative measure of effort, and a **Sprint** is a fixed period of work. The scope covers the Service Catalog booking flow, fare logic, payment options, and the QR ticket widget; it does not include a separate ticket database, Flow Designer automation, or RITM number tracking.

1. Product Backlog, Sprint Planning, Stories & Story Points

Sprint	Functional Requirement (Epic)	User Story No.	User Story / Task	Story Points	Priority	Team Members
Sprint-1	Station & Catalog Setup	USN-1	Create the Metro Station's Details table and add the station records.	3	High	Team
		USN-2	Create the Book A Metro Ticket catalog item and its variables.	5	High	Team
		USN-3	Set up the Starting From and Going To station references.	2	High	Team
	Fare Automation	USN-4	Write and test the fare calculation client script.	5	High	Team
		USN-5	Add same-station validation and handle the fare fields.	3	High	Team
Sprint-2	Payment	USN-6	Configure the UPI, Card, and Others payment choices.	2	High	Team
	Payment	USN-7	Set up the UI policy that shows Enter Payment Mode conditionally.	2	Medium	Team
	QR Ticket	USN-8	Build the Metro QR Widget and the QR display script.	5	High	Team
Sprint-3	Testing & Deployment	USN-9	Run end-to-end testing of booking, fare, payment, and QR display.	5	High	Team
	Testing & Deployment	USN-10	Prepare the update set and complete deployment.	3	High	Team

Sprint Schedule

Sprint	Total Story Points	Duration	Sprint Start Date	Sprint End Date (Planned)	Story Points Completed (Planned)	Sprint Release Date (Planned)
Sprint-1	18	6 Days	15 Sep 2026	20 Sep 2026	18	20 Sep 2026
Sprint-2	9	4 Days	21 Sep 2026	24 Sep 2026	9	24 Sep 2026
Sprint-3	8	4 Days	25 Sep 2026	28 Sep 2026	8	28 Sep 2026

2. Planning Logic, Velocity & Burndown


Story points use the scale 1, 2, 3, and 5, where 1 means very easy and 5 means difficult.

Planned total story points = $18 + 9 + 8 = 35$. **Planned average velocity** = $35 / 3 \approx 11.7$ story points per sprint.

Burndown approach: each sprint begins with remaining points equal to that sprint's backlog. As stories are finished, the remaining points fall towards zero. The actual burndown should be updated using the team's real completion data.

Sprint	Planned Points	Expected Remaining at Start	Target Remaining at End
Sprint-1	18	18	0
Sprint-2	9	9	0
Sprint-3	8	8	0

Planned Burndown Chart

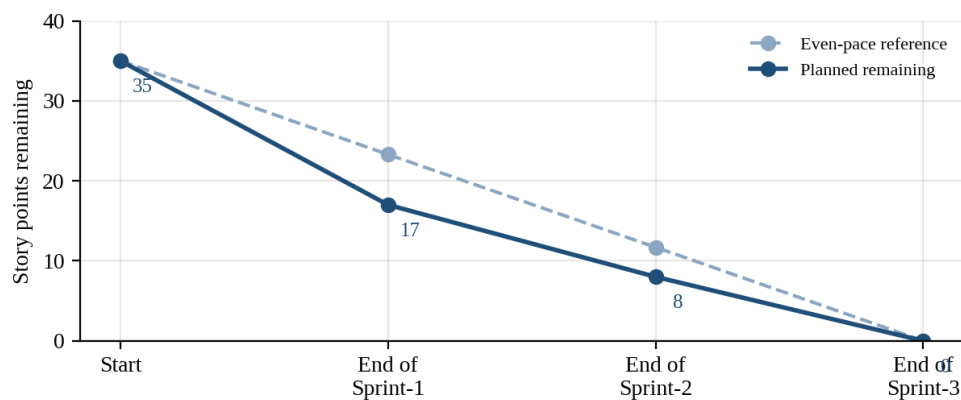

Planning Assumptions

- The project is carried out by a student team in a ServiceNow development environment.
- The scope is limited to the Service Catalog booking form, client-side fare and validation logic, payment selection, and the QR ticket widget; there is no separate ticket database, Flow Designer flow, or RITM number tracking in this project.
- The dates form a planned schedule for documentation purposes and can be changed if the team followed different actual sprint dates.
- Actual velocity and burndown values should replace the planned figures if the mentor asks for them.
